

2019 Bond Program

Status Report

Dubose

Intermediate

- Contractor has mobilized
- Temporary Fencing & erosion control
- Site Demolition & Excavation
- Street Closure for Water & Sewer





William Adams

Middle School

- Contractor Mobilized
- Construction Office Trailer Placed
- Building Permit Received
- Site Demolition-Concrete and Light Poles
- Canopy Removal Started





Noonan Elementary

- Contractor mobilized
- Project Sign Installed
- Temporary Fencing Completed
- Erosion Controls in Place





Saenz Elementary

- Contractor Mobilized
- Project Sign Installed
- Temporary Fencing in Place
- Erosion Controls in Progress





Schallert Elementary

- Contractor mobilized
- Project Sign Installed
- Temporary Fence in Place
- Site Demolition in Progress
- Clearing & Excavation Started






High School Parking Lot Improvements



High School Roofing Project

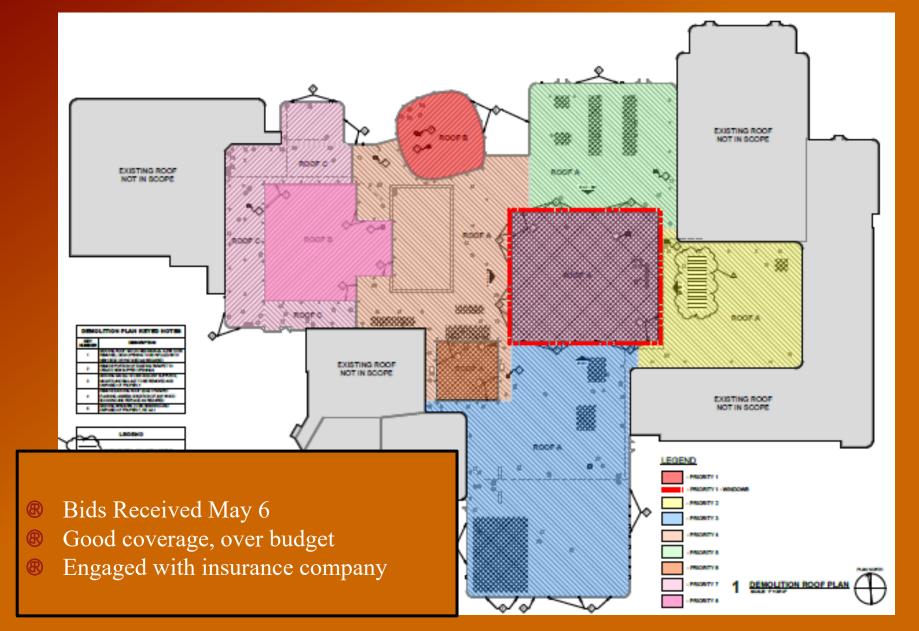



Bond Cost Update



2019 Bond Program Financial Summary



Project	Bond Budget		Committed Costs		Change Orders		Total Committed		Budget Balance		Expenditures to Date		Expenditure Balance	
Dubose Campus Addition	\$ 2,337,082	\$	2,172,589	\$	-	\$	2,172,589	\$	164,493	\$	150,587	\$	2,022,002	
WAMS Campus Addition	\$ 5,842,705	\$	4,691,867	\$		\$	4,691,867	\$	1,150,838	\$	366,464	\$	4,325,403	
Noonan Campus Addition	\$ 2,921,353	\$	2,742,140	\$		\$	2,742,140	\$	179,213	\$	198,339	\$	2,543,801	
Saenz Campus Addition	\$ 2,921,353	\$	2,842,408	\$	-	\$	2,842,408	\$	78,944	\$	199,836	\$	2,642,572	
Schallert Campus Addition	\$ 2,921,353	\$	2,928,912	\$		\$	2,928,912	\$	(7,560)	\$	201,990	\$	2,726,922	
High School Roofing & Parking Lots	\$ 3,037,944	\$	215,531	\$		\$	215,531	\$	2,822,413	\$	145,008	\$	70,523	
Miscellaneous	\$ 808,211	\$	371,754	\$		\$	371,754	\$	436,457	\$	119,795	\$	251,958	
TOTALS	\$ 20,790,000	\$	15,965,201	\$	-	9	15,965,201	\$	4,824,799	\$	1,382,020	\$	14,583,181	



Questions?
